



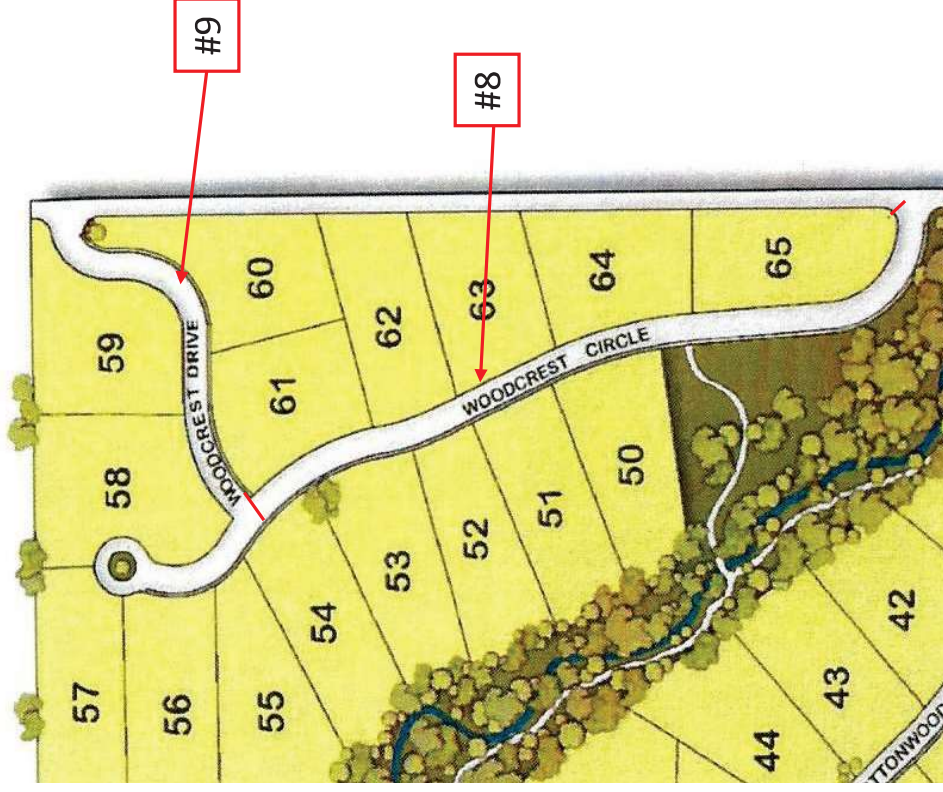


2021 PLAN Step #1

- Complete what we planned to do in 2020
- Remove Trees & Vegetation causing issues
- Drainage Grading
- Dig Outs on selected Spots
- Heavy Duty Crack Seal
- Spray Seal Road Surfaces
- Work is scheduled to start June 7th 2021

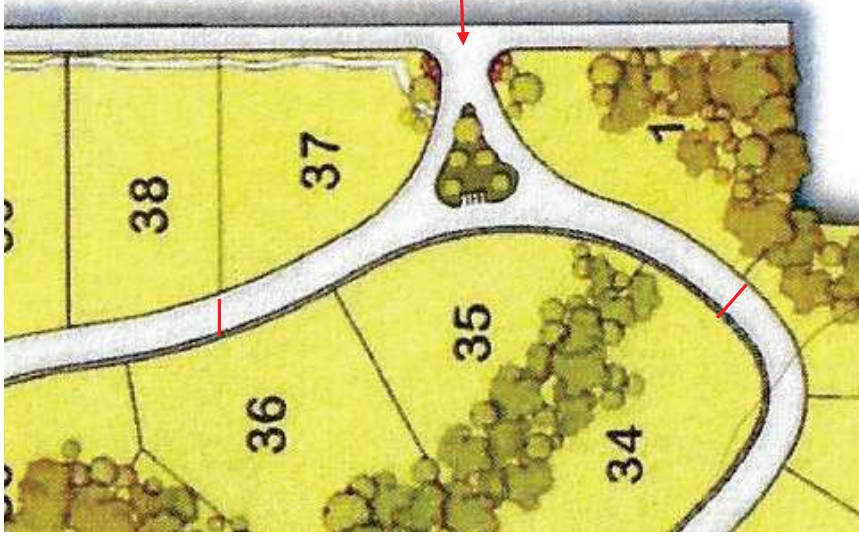

2021 PLAN Step #2

- Redesign Entrance Area paved surfaces to eliminate future drainage issues
- Drainage Grading
- Edge Drain installation where Needed
- Mill 2" of remaining road surface
- Dig Outs on selected Spots
- Overlay with 2" of Recycled Asphalt
- Work is scheduled to start June 14th 2021

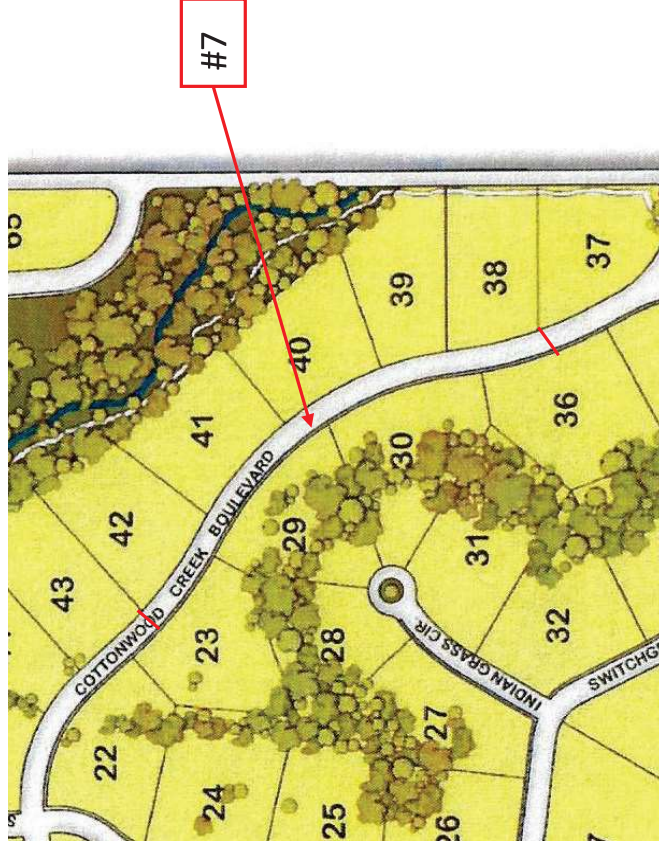

2021 PLAN Step #3

- Drainage Grading
- Repair New House Construction Damage
- Mill 2" of remaining road surface
- Dig Outs on selected Spots
- Overlay with 2" of Recycled Asphalt
- Work is scheduled to start June 14th 2021

2021 PLAN Step #4

- Misc. Drainage Grading
- Dig Outs on selected Spots (Primarily Circles)
- Add Traffic Calming Feature in Section #2 as requested
- Heavy Duty Crack Seal
- Spray Seal Road Surfaces
- Work is scheduled to start June 21th 2021

